


Lake Michigan Water Main Project – Update 10/12/15

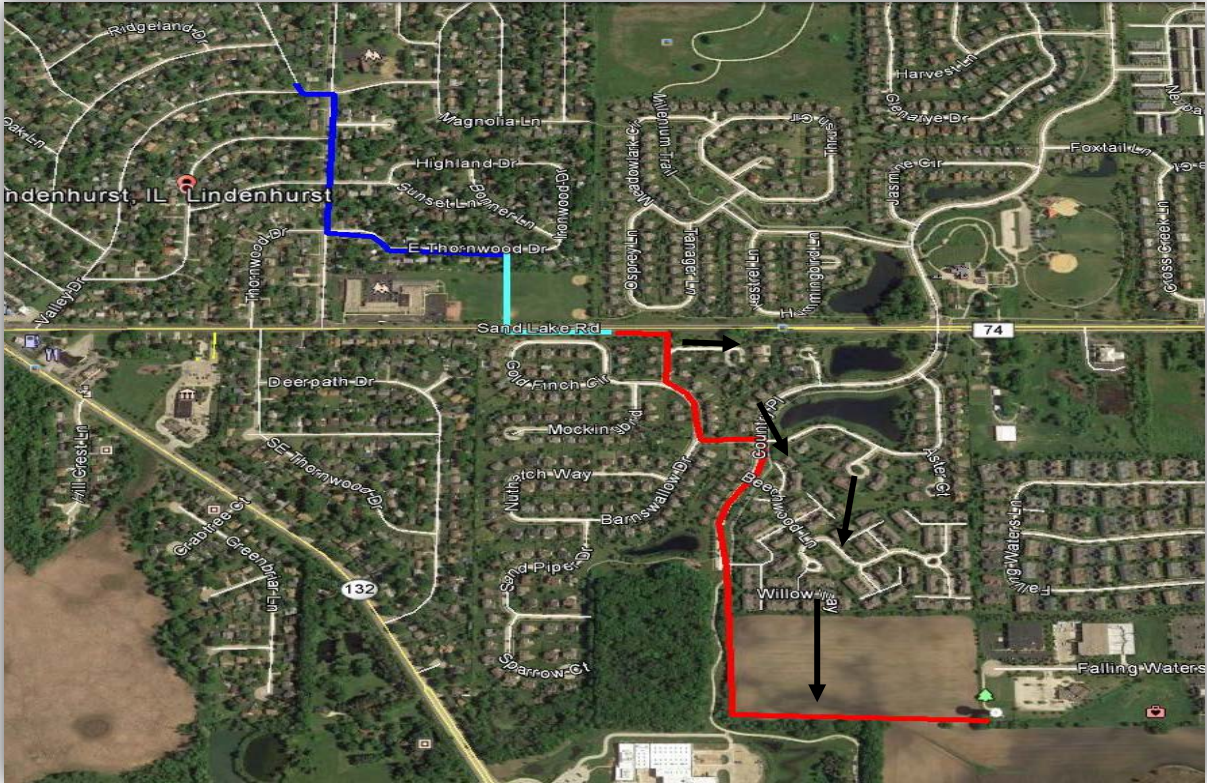

- Blue** – Installed, pressure tested, chlorinated and passed
- Light Blue** – Installed, pressure tested, chlorinated, waiting on results
- Red** – Remaining path of installation

Bench Marks

- The blue section of the project has been pressure tested, chlorinated, and cleared for use
- Water services along the blue line have been transferred from the old main to the new main
- Portions of the new main have been connected to the existing water main in preparation of abandonment
- Roads on E. Thornwood Drive, Ironwood Drive, Bonner Lane, Sunset Drive, and Highland Drive have been removed in preparation of new asphalt

A Look Ahead

- Remaining existing water main to be connected
- Binder and Surface to be placed for paved roads
- Work to commence in Country Place Subdivision
