



Village of Lindenhurst Construction Update – May 5, 2016

Phase 1 Watermain

2015 Project – This project started the 16” diameter watermain connection between the Village’s two water towers. Seeding of the turf areas has started and corrective paving is under way now that bituminous materials are available.




2016 Project – Restoration is under way! The asphalt plants have just opened and paving has started on Sand Lake Road, Valley Drive, and Old Elm Road. Valley Drive at Sand Lake Road should be fully open next week. Old Elm Road ditch and driveway restoration will be started now that the first layer of asphalt is in.



Sand Lake Rd



Valley Dr

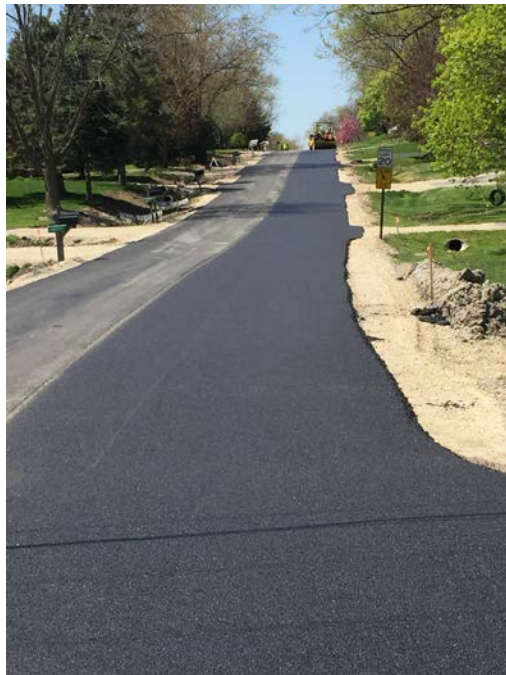

Old Elm

Phase 2 Watermain Project

The contractor, DiMeo Bros, Inc., has installed almost all of the watermain on Beck Road and services are being transferred over to the new watermain. Work on Beck Road at Grass Lake Road is pending special permits from Lake County. The new watermains have been installed on west Sunset Lane, Briar Lane, and Thornwood Drive. Services are now being extended to the property line. The new watermain from Robincrest Lane to the NW Watertower is in under the bikepath and restoration is almost complete. The Forest Preserve entrance is again open for use!



400 Block Beck Rd



Thornwood Dr



Forest Preserve Entrance

Beck Road Construction Project

The road reconstruction project extends from Sand Lake Road to Grass Lake Road. The project is being built with 80% federal funds and is matched with 20% Village funds. Bids were opened in Springfield on April 22 with Berger construction the low bidder at just over \$3,000,000. The project start is about 6-8 weeks out and additional updates are coming.



Lake Michigan Water Receiving Facility and Pumping Station

Site grading has started for the Reservoir (foreground) and Pumping Station. Work will continue this year. Ground breaking for the pump station is scheduled for next week.

